

AgilePgM™ mind map

http://www.mindmeister.com/456109763


AgilePgM™

An agile (iterative, incremental and adaptive) programme management method created by DSDM® Consortium in 09.2014.

AgilePgM™ is a general programme management method which can be used for managing programmes within any business domain. AgilePgM™ can be easily combined with agile project management methods such as AgilePM®, DSDM® or with traditional such as PRINCE2®.

AgilePM®, DSDM® and Alt® are registered trademarks of Dynamic Systems Development Method Limited in the United Kingdom and other countries. AgilePgM™ is a trade mark of Dynamic Systems Development Method Limited.

Phases

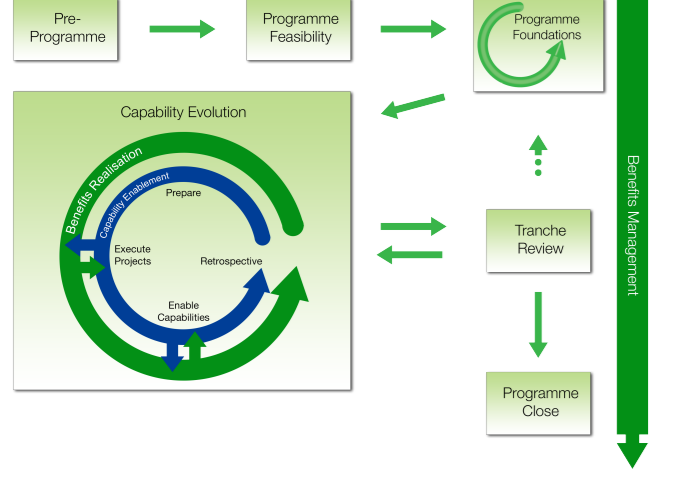

	Pre-Programme
	Programme Feasibility
	Programme Foundations
	Capability Evolution
	Tranche Review
	Programme Close

Products

Business-focused products
Programme management products
Outputs, Capabilities, Benefits
Benefits management products

Roles



BPO	Business Programme Owner	Programme Management
BCOs	Business Change Owners	
PM	Programme Manager	
PCA	Programme Change Architect	Capability Delivery Team
PTA	Programme Technical Architect	
PTs	Project Teams (represented by Project Manager)	
SEC	Stakeholders Engagement Coord.	Others / Supporting
CAs	Change Agents	
Ss	Specialists	
PSO	Programme Support Office	



- | | | | | | |
|---|--|--|--|--|---|
| <ul style="list-style-type: none"> Describe business transformation Identify Business Programme Owner (PBO) and Business Change Owners (BCOs) Confirm alignment of programme vision with business strategy Scope, Plan, Resource Programme Feasibility phase Check if programme is worth pursuing to Programme Feasibility phase | <ul style="list-style-type: none"> Confirm programme is consistent with business strategy and potentially achievable Refine outline vision of programme Outline high-level benefits of business transformation Produce initial outline costs for the programme Confirm programme structure Develop outline plan for Programme Foundations Develop outline governance strategy Assess organisation readiness for use of Agile techniques on the programme | <ul style="list-style-type: none"> Baseline programme vision Create initial Business Architecture Model Define initial Roadmap for realising vision Define and prioritise the high-level benefits and capabilities Confirm the Business Case for the programme Establish governance model that is Agile Develop Programme Plan Describe, assess and manage risk Identify and categorise key stakeholders Plan initial tranche(s) Obtain approval to proceed to first tranche Gain funding for at least the first tranche | <ul style="list-style-type: none"> Plan initiate and execute projects to deliver the capabilities required for realisation of benefits Iteratively and incrementally enable consistent subsets of capabilities into the live organisation Deliver capabilities as soon as possible through projects with delivering outputs regularly and often Run projects within tranches (tranches can be overlapping) Measure the benefits being realised through the capabilities Benefits realisation benchmarks and assesses capability enablement | <ul style="list-style-type: none"> Confirm the sufficient capability has been delivered for the tranche Assess the on-going viability of the programme Plan next tranche in sufficient detail Review the programme and update plans and other Programme Foundations products as necessary based on experiences from the current tranche Review lessons learnt | <ul style="list-style-type: none"> Confirm that sufficient capability has been delivered Close the programme Gather lessons learnt for the future initiatives Review the programme against its vision and Business Case |
|---|--|--|--|--|---|

	Pre-Programme										Programme Feasibility										Programme Foundations										Capability Evolution										Tranche Review										Programme Close																			
	Programme Management Team (PMT)		Capability Delivery Team (CDT)				Supporting				Programme Management Team (PMT)		Capability Delivery Team (CDT)				Supporting				Programme Management Team (PMT)		Capability Delivery Team (CDT)				Supporting				Programme Management Team (PMT)		Capability Delivery Team (CDT)				Supporting																																	
	BPO	BCOs	PM	PCA	PTA	PTs	SEC	CAs	Ss	PSO	BPO	BCOs	PM	PCA	PTA	PTs	SEC	CAs	Ss	PSO	BPO	BCOs	PM	PCA	PTA	PTs	SEC	CAs	Ss	PSO	BPO	BCOs	PM	PCA	PTA	PTs	SEC	CAs	Ss	PSO	BPO	BCOs	PM	PCA	PTA	PTs	SEC	CAs	Ss	PSO	BPO	BCOs	PM	PCA	PTA	PTs	SEC	CAs	Ss	PSO										
Business Case	O/CU C C C C C C C C C C										Refined										Refined & Baseline										Used & Updated										Used & Updated										Archived																			
Vision Statement	O/CU CU CU C C C C C C C C										Additional contribution: Various stakeholders										Refined & Baseline										Used & Updated										Used & Updated										Archived																			
Business Architecture Model (BAM)	O C CU C C C C C C C C C C										Additional contribution: Programme Team; Additional support: experts in the process, organisational structure, technology and information										Used & Updated										Used & Updated										Archived																													
Programme Plan	O/CU Additional contribution: Various Stakeholders; Additional support: Programme Team and Business and Technical experts										Refined & Baseline										Used & Updated										Used & Updated										Archived																													
Roadmap	CU CU O/CU CU CU CU CU CU CU CU CU CU										Additional support: Programme Team and Business and Technical experts										Used & Updated										Used & Updated										Archived																													
Tranche Plan	CU CU O/CU CU CU C CU C C C C										Additional support: Programme Team and Business and Technical experts										Used & Updated										Initiated & Refined & Baseline (for next tranche) Archived (for previous tranche)										Archived																													
Tranche Review Record	O/CU Additional contribution: Various Stakeholders										Used & Updated										Used & Updated										Used & Updated										Archived																													
Programme Control Pack	O/CU Additional contribution: Various Stakeholders										Used & Updated										Used & Updated										Used & Updated										Archived																													
Programme Risk Log	C C O/CU C C C C C C C C C C										Additional contribution: Various Stakeholders										Used & Updated & Refined										Used & Updated & Refined										Used & Updated & Refined										Archived																			
Programme Issue Log	C C O/CU C C C C C C C C C C										Additional contribution: Various Stakeholders										Used & Updated & Refined										Used & Updated & Refined										Used & Updated & Refined										Archived																			
Communications Log	C C O/CU C C C C C C C C C C										Additional contribution: Various Stakeholders										Used & Updated & Refined										Used & Updated & Refined										Used & Updated & Refined										Archived																			
High Level Projects Status	C CU O/CU C CU CU C C C C C C										Additional contribution: Various Stakeholders										Used & Updated & Refined										Used & Updated										Used & Updated										Archived																			
Stakeholder Engagement Strategy	O/CU CU CU C C C C C CU C C										Additional contribution: Various Stakeholders										Refined & Baseline										Used & Updated										Used & Updated										Archived																			
Communication Plan	O CU CU C C C C C C C C C C										Additional contribution: Various Stakeholders										Used & Updated										Used & Updated										Initiated & Refined & Baseline (for next tranche) Archived (for previous tranche)										Archived																			
Governance Strategy	O/CU CU CU Additional contribution: Various Stakeholders										Updated & Refined & Baseline										Used & Updated										Used & Updated										Used & Updated										Archived																			
Capabilities	O/CU CU CU C C C C C CU C C										Additional contribution: Various stakeholders										Used & Updated										Used & Updated										Used & Updated										Archived																			
Benefits	O CU CU C C C C C C										Additional contribution: Various Stakeholders										Used & Updated										Used & Updated										Used & Updated										Archived																			
Prioritised Benefits Definition	O/CU CU CU CU C C C C C C C C										Additional contribution: Various Stakeholders										Refined										Refined & Baseline										Used & Updated										Used & Updated										Archived									
Benefits Assessment	O/CU CU CU CU C C C C C C C C										Additional contribution: Various Stakeholders										Used & Updated										Used & Updated										Used & Updated										Archived																			
Benefits Realisation Plan	O/CU CU CU CU C C C C C C C C										Additional contribution: Various Stakeholders										Refined										Refined & Baseline										Used & Updated										Used & Updated										Archived									

Responsibilities

O	Owned by
A	Agreed by
CU	Compiled and
C	Consulted with
